



409 E. Pflugerville Parkway, Pflugerville, Texas 78660

Construction Update: Sept 29 – October 12, 2025

START DATE: MARCH 21, 2025

PROJECT MANAGER: RICK ROZENHART | 512.845.5466

SITE SUPERINTENDENT: LEO MARTINEZ | 512.587.5290



Current Week

Monday, September 29, 2025	Setting storefront glazing; installing soffit at perimeter of standing seam roof; inspection for secondary to building; trenching for u/g electrical to light poles; backfilling throughout
Tuesday, September 30, 2025	Setting storefront glazing; brazing AHU line sets; installing soffit at perimeter of standing seam roof
Wednesday, October 1, 2025	Setting storefront glazing; brazing AHU line sets; installing soffit at perimeter of standing seam roof
Thursday, October 2, 2025	Setting storefront glazing; installing soffit at perimeter of standing seam roof; relocating interior wall to accomodate scale
Friday, October 3, 2025	Setting storefront glazing; installing standing seam roof panels; pier drilling for transformer pad
Saturday, October 4, 2025	No Work Scheduled
Sunday, October 5, 2025	No Work Scheduled

One-Week Look Ahead

Monday, October 6, 2025	Setting storefront glazing; BUILDING DRIED IN , formwork / rebar for transformer pad
Tuesday, October 7, 2025	Installing gypsum board; ONCOR inspection of transformer pad; setting coping cap at parapets
Wednesday, October 8, 2025	Installing gypsum board; concrete placement at transformer pad; drilling for light pole foundations; setting coping cap at parapets
Thursday, October 9, 2025	Installing gypsum board; form and rebar for light pole bases; spray foam insulation
Friday, October 10, 2025	Installing gypsum board; form and rebar for light pole bases; spray foam insulation
Saturday, October 11, 2025	No Work Scheduled
Sunday, October 12, 2025	No Work Scheduled

Progress Photos

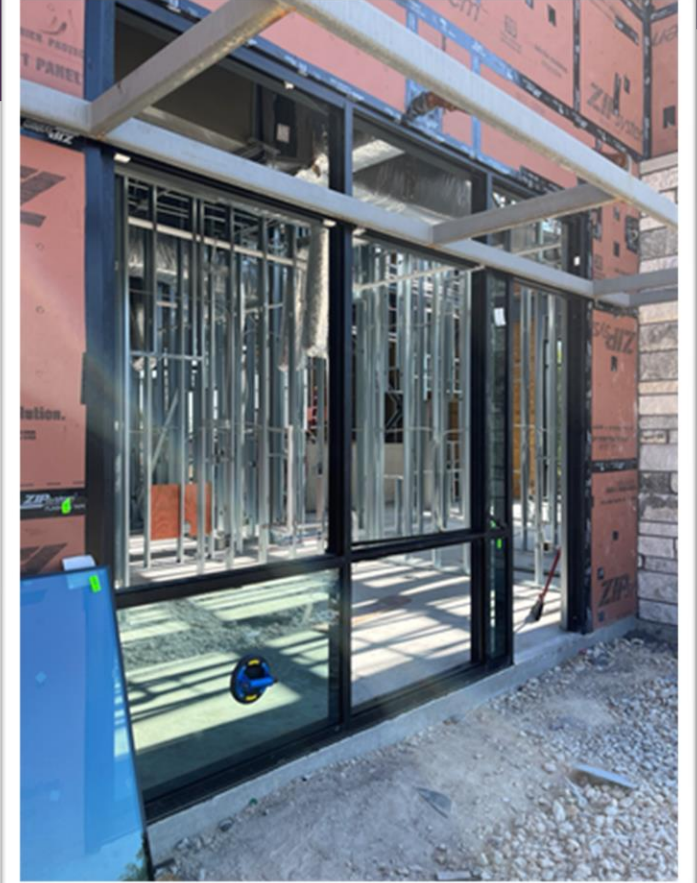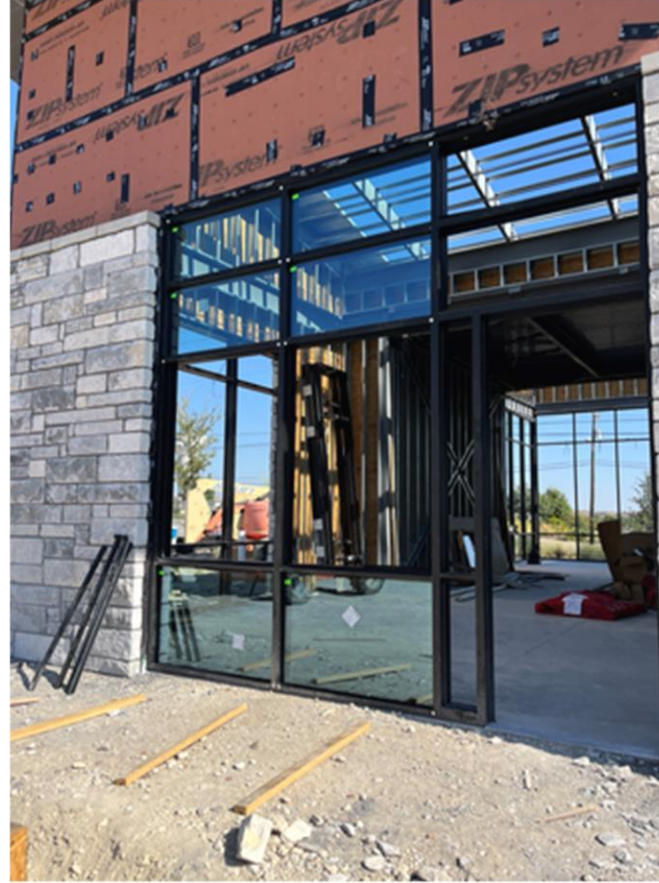

Progress Photos

